Forge Conductor - Dossier

Derived reading copy. Markdown remains the source of record. No source file is modified by this build.

Ridgeboundia / DeerFlow Forge Agent Program

Status: research + execution evidence + implementation plan. **No production repair has been applied.** Date: 2026-11-05. Owner: Riley.

This is the master entry point for the agent-harness work. It explains what exists, what is broken, what we are building, the six integrations, eight Python changes, eight agent/tool/skill changes, the goal evaluation, and how to read the evidence without drowning in it.

> **Read next:** [`GOALS.md`](GOALS.md) -> [`ARCHITECTURE.md`](ARCHITECTURE.md) ->
> [`execution-wave/09-GOAL-GAP-PLAN.md`](execution-wave/09-GOAL-GAP-PLAN.md) -> [`PLAIN-ENGLISH.md`](PLAIN-ENGLISH.md).
> Diagrams: [`diagrams/index.html`](diagrams/index.html).

---

1. The outcome we are building

A hosted **Forge Conductor** on the existing DeerFlow 2.2 + DeepSeek V4.1 Flash runtime that can:

1. take a print/vector brief;
2. choose exact Craft command ids from a pinned catalogue;
3. run on copies through a typed CLI/MCP gateway;
4. verify artifact hashes, dimensions/DPI, domain gates, an independent render and a blind visual critic;
5. record a hash-chained episode with evidence;
6. propose a lesson/skill only after repeated verified success and human approval;
7. never publish to the storefront without explicit human approval.

The first release is a **production operator under human art direction**, not an autonomous artist, not a new generic superagent, and not a claim of "better than human."

2. What we know now (the short truth)

Area	Finding
VPS	2 vCPU / 7.9 GB / 36 GB free, no GPU/display; DeerFlow 2.2 already running
Model	`deepseek-flash` ("DeepSeek V4.1 Flash"), 1,048,576 ctx, 8,192 output; key validity unverified
Craft apps	VectorCraft 0.21.1 + PhotoCraft 0.20.2 installed; Film/Design/Effect **absent**
Execution	`/opt/pod-pipeline/bin/*-cli` are **stubs exiting 127**; `routes.py` argv is invented
MCP	Craft MCP works standalone (33/26 tools) but is **not registered** in DeerFlow
Persistence	`pod` DB empty/schema-only; **no** episode/action/eval/skill tables
Learning	DeerMem facts + skill-evolution host exist; **no** full learner or quality evaluation
Publish	`fourthwall_template_id` unset for all five products; no approval queue
Evidence	README's live-E2E claim is historical/unreproducible in the current state
Assets	39 skills, 400 answers, 6 examples, 8 validated diagrams, 131-file package

The key sentence: **the model/harness is present; the Craft execution path and learning evidence are not.** Phase 0 starts there.

3. Six integrations

#	Integration	What it connects	Why it is needed	Acceptance gate
I1	**Craft launcher + argv contract**	`/opt/craft/*/bin` -> `deploy/craft-bin` -> `routes.py`	The pipeline cannot execute a Craft command today	one real VectorCraft trace + one real PhotoCraft retouch
I2	**Craft MCP bridge**	VectorCraft/PhotoCraft stdio MCP -> DeerFlow `mcpServers`	Gives the agent native 33/26-tool surfaces without shell guessing	`tools/list` + `command_batch`; dependent PhotoCraft calls awaited
I3	**Forge Conductor service**	Console/DeerFlow -> `forge-conductor:8092` -> queue/ledger	Owns planning, budgets, episode state and recovery	replay one episode from ledger; no source mutation
I4	**Evidence verifier + blind critic**	artifacts -> gates -> render -> tile metrics -> critic	Exit 0/`ok:true`/screenshots are not proof	5-check composite + human rubric; missing evidence = UNVERIFIED
I5	**Human approval + publish**	Forge approval -> Fourthwall product state	Publishing is irreversible and currently misconfigured	approval bound to artifact hash; template ids set; no auto-publish
I6	**Learning + evaluation loop**	episodes -> retrieval -> candidate skill -> regression -> active	"Learns" must mean a measured, reversible change	calibrated promotion + A/B; null result disables memory

I1 - Launcher + argv contract (P0)

- **Files:** `blueprint/files/deploy/craft-bin/*-cli`, `blueprint/files/pod_pipeline/routes.py`, `deploy/setup-pipeline.sh`.
- **Measured contract (do not revert to the old ASSUMPTION):**
- VectorCraft: `run --in F --cmd select.all --cmd imageTrace.make --params '{"params":{...}}' --cmd imageTrace.expand --export out.svg`; export does **not** create parent dirs.
- PhotoCraft: `run FILE|--new --cmd ID --params J --out F`; creates parent dirs.
- **Refusal:** absent app -> `E_TOOL_NOT_INSTALLED`, not a fake trace.
- **Rollback:** restore the original launchers and `routes.py` from backup.

I2 - Craft MCP bridge (P0)

- **Files:** DeerFlow `extensions_config.json`; optional stdio bridge; read/write roots.
- **Rules:** VectorCraft `mcp --headless --automation-read/write-root`; PhotoCraft `mcp` without `--headless` + roots; await each `tools/call` (PhotoCraft can interleave).
- **Gate:** `tools/list` returns 33/26; a real batch produces an artifact.

I3 - Forge Conductor service (P1)

- **Files:** new `blueprint/files/forge/*`, `sql/schema_forge.sql`, `deploy/systemd/forge-conductor.service`, `deploy/systemd/forge-worker.service`.
- **DB:** 13 tables (episode, event, handoff, tool_call, artifact, gate, critique, eval, job, skill, budget, approval, transition).
- **Gate:** 18 SQL assertions, 33 Python tests, SKIP LOCKED two-worker test; episode replay.

I4 - Evidence verifier + blind critic (P1)

- **Files:** `forge/verifier.py`, `forge/critic.py`, gate adapters.
- **Ladder:** process -> artifact/hash -> domain gates -> independent render -> tile/crop metrics -> blind critic -> human.
- **Measured:** global SSIM catches 7/15; tile-min 13/15 but 3/4 false alarms; 5-check composite **15/15 recall, 0/4 false alarms** on the synthetic corpus.
- **Gate:** missing metric -> `UNVERIFIED`; critic cannot override a failed gate.

I5 - Human approval + publish (P1)

- **Files:** `forge/approval`/`forge_publish.py`, `config/products.json`, Fourthwall client.
- **Rules:** approval table binds to artifact hash + scope; template/area validated; no autonomous publish; product state read back.
- **Gate:** approval reused -> blocked; missing template -> named refusal; no store mutation in tests.

I6 - Learning + evaluation (P2/P3)

- **Files:** `forge/memory.py`, `forge/promotion.py`, `forge/eval.py`, DeerFlow memory/skill config.
- **Rule:** L1/L2 only (retrieval/skills), no fine-tune/RL. Promotion requires a declared horizon, Wilson lower bound above baseline, golden regression and human approval. **3/3 is not enough** (Wilson LB 0.4385; the old rule was rejected by simulation).
- **Gate:** A/B on held-out goldens; null result disables memory; rollback pointer.

4. Eight small Python enhancements

These are **planned**, not applied. Each is written to be independently testable.

#	File / function	Change	Test
P1	`pod_pipeline/routes.py` `trace_step` / `raster_fallback_step`	replace invented `trace`/`--input` argv with measured `run` contracts	`test_routes.py` + one live trace/retouch
P2	`pod_pipeline/orchestrator.py` `_run_step` / preflight	check binary exists, app version, catalogue hash; `E_TOOL_NOT_INSTALLED`	missing-binary error path
P3	`tools/craft_trace.py` gate assembly	make `retyped_text_present` non-vacuous; record artifact path/hash; gate status before/after save	0-box text fixture must fail; text fixture must pass
P4	`tools/prep_print_art.py` report	stop treating `ok:true` as a pass; expose warning-only upscale and coverage; add `verdict`	3.6x upscale test must be `refused_for_print`
P5	`pod_pipeline/runner.py` / orchestrator	hash inputs before/after; flag source mutation; atomic artifact copy	mutate a fixture; episode must fail
P6	`pod_pipeline/db.py` / new `forge/repo.py`	idempotency key, duplicate replay, unique constraints, queue lease	duplicate call = one effect; crash/requeue
P7	`pod_pipeline/worker.py`	lease expiry/reaper/recovery with bounded scans	kill worker mid-run; reclaim once
P8	`pod_pipeline/orchestrator.py` / new `forge/cost.py`	persist token/cost per step/episode; enforce caps	cap exceeded returns named refusal, no silent truncation

5. Eight agent/tool/skill enhancements

These are changes to how agents use the stack; most are documentation/protocol now, code/tooling later.

| # | Skill/tool | Enhancement | Why |

|---|---|---|---|

| **A1** | `craft-agent-operator` | mandatory evidence contract + no screenshot/exit-code proof + episode record | prevents "it looked good" shipping |

| **A2** | `agent-learning-loop` | calibrated promotion/demotion/regression, corrected 3/3 rule | simulation showed the original rule cannot promote |

| **A3** | `visual-verification-critic` | 5-check composite, black+white render, region/tile evidence | global SSIM misses 4% defects |

| **A4** | `forge-harness-architect` | Phase 0 app/binary preflight; VC/PC-only scope | prevents designing for absent apps |

| **A5** | `harness-code-adapter` | donor provenance/pin, adapter contract, no verbatim code | code stitching without a fork |

| **A6** | `research-corpus-navigator` | map 400 answers + claim/errata; one-slice loading | stops context flooding |

| **A7** | `craft-mcp-drive` | await dependent calls; auth/loopback; stdio vs HTTP gap | PhotoCraft interleaving + exposed MCP |

| **A8** | `apparel-print-master` / publish skills | bind approval to artifact hash; template/rights preflight | no irreversible publish on a stale master |

6. Phase plan and gates

| Phase | Deliverable | Gate |

|---|---|---|

| **0** | launchers, argv, MCP registration, 10 goldens, README/AGENTS correction | one real trace + retouch; no stub; expected artifacts |

| **1** | Forge skeleton, verifier, approval, queue | replay from ledger; duplicate/refusal/crash tests |

| **2** | blind critic, tile metrics, human rubric | 15/15 synthetic recall / 0/4 false alarms; missing -> UNVERIFIED |

| **3** | retrieval + A/B | measured gain or null; memory disabled on null |

| **4** | skill promotion/rollback | calibrated horizon + regression + human; rollback drill |

| **5** | print + second app + 50 goldens | no unsafe publish; measured cost |

| **6** | security/backup/hardening | restore drill; key metadata check; MCP auth |

Estimate: 6-10 weeks for Phase 0-2; this is an `ESTIMATE`, not a measured schedule.

7. Goal evaluation (summary)

| Goal | Status | Evidence | What moves it |

|---|---|---|---|

| G1 execute Craft | **BLOCKED** | stubs + invented argv | I1/P1/P2 |

| G2 native tools | **PARTIAL** | MCP works standalone, not registered | I2/P6 |

| G3 verify quality | **PARTIAL** | gates exist, can lie; no critic integration | I4/P3/P4 |

| G4 learn | **NOT STARTED (L0)** | no ledger/eval | I3/I6/P6-P8 |

| G5 host on VPS | **FEASIBLE** | 2 vCPU, model running | I3 + caps |

| G6 safe publish | **BLOCKED** | no approval, templates unset | I5/A8 |

| G7 truth | **IMPROVING** | claim register; README correction pending | docs/ERRATA |

Full detail: [`GOAL-EVALUATION.md`](GOAL-EVALUATION.md).

8. What is possible / what is best

Possible now: repair the execution path, run one real trace/retouch, record evidence, verify dimensions/DPI/gates, build the ledger/queue, and prove replay/idempotency. **Best first move:** I1 + I2 + I3, not GUI or training.

Not possible now: all Craft apps, autonomous publish, fine-tuning, RL, "better than human," or a production claim that the current agent learns.

Best architecture: DeerFlow 2.2 as front door/runtime + Forge Conductor as third plane + native Craft CLI/MCP + Postgres ledger/queue + DeerMem facts + versioned skills. Do not build a new generic harness or vendor a whole donor repo.

9. Evidence and files

```
| Item | Where |
|---|---|
| Goals/non-goals | [`GOALS.md`](GOALS.md) |
| Architecture | [`ARCHITECTURE.md`](ARCHITECTURE.md) |
| Integration map | [`INTEGRATIONS.mmd`](INTEGRATIONS.mmd) + SVG/PNG |
| Eight validated diagrams | [`diagrams/`](diagrams/index.html) |
| Goal->code gap + decision plan |
[`execution-wave/09-GOAL-GAP-PLAN.md`](execution-wave/09-GOAL-GAP-PLAN.md) |
| Recon ledger | [`execution-wave/RECON-LEDGER.md`](execution-wave/RECON-LEDGER.md) |
| Claim register | [`execution-wave/10-CLAIM-REGISTER.md`](execution-wave/10-CLAIM-REGISTER.md) |
| Independent verification |
[`execution-wave/08-VERIFICATION-INDEPENDENT.md`](execution-wave/08-VERIFICATION-INDEPENDENT.md) |
| First 200 | [`REPORT.md`](REPORT.md) |
| Second 200 | [`wave2/08-200-QUESTIONS.md`](wave2/08-200-QUESTIONS.md) |
| Six examples | [`examples/`](examples/README.md) |
| PDF catalogue | [`PDF-CATALOGUE.md`](PDF-CATALOGUE.md) |
| Plain English | [`PLAIN-ENGLISH.md`](PLAIN-ENGLISH.md) |
```

10. Truth rules

- A design is not an implementation; `PROPOSED` is not `VERIFIED`.
- Exit 0, `ok:true`, a screenshot or a README claim is not proof.
- The 400 answers are a fixed corpus; re-fetch before changing policy.
- No production file/DB/service has been changed by this research wave.
- "Better than human" is unsupported; no blind study exists.
- FilmCraft/DesignCraft/EffectCraft are absent and out of the current scope.
- The key is configured by name only; validity is unverified until the zero-spend metadata check.

11. Next action

Approve **Phase 0**. Apply I1/I2 on a staging copy, run one real trace and one real retouch, write the evidence to the ledger, then decide whether Phase 1 is worth building. Do not start with fine-tuning, GUI automation or autonomous publishing.

Architecture

Status: target architecture + as-is architecture. Design, not deployed. Date: 2026-11-05.

This document answers: where the agent lives, what it calls, what it owns, what it must never own, how evidence flows, and how a run is recovered. For the short version see [`README.md`](README.md).

---


1. As-is (what is actually running)

```
Operator/SSH
?
??? console (127.0.0.1:8091) ?? pure viewer, no agent loop
??? pod-mcp (0.0.0.0:8765) ?? 3 tools, unauthenticated
? ??? pod worker/orchestrator ?? deterministic Python pipeline
? ??? /opt/pod-pipeline/bin/*-cli ?? STUBS, exit 127
?
??? DeerFlow 2.2 gateway/UI ?? model deepseek-flash, subagents, DeerMem, checkpoints
??? only registered MCP: forge (3 pipeline tools)
```

Real Craft binaries exist at `/opt/craft/vectorcraft/.../vectorcraft-cli` and `/opt/craft/photocraft/.../photocraft-cli`; their MCP servers work standalone but are not registered.
No episode/eval/skill tables exist in `pod`; DB is empty.

The pipeline's argv is invented (`routes.py:73-96`), so the chain breaks at the first Craft step.
The README's live-E2E sentence is historical, not current.

2. Target (Forge Conductor)




```
DeerFlow 2.2 (front door, sessions, subagents, DeerMem, checkpoints)
? TaskEnvelope (brief, rights, app/version, output contract, gates, budget)
????????????????????????????????????????????????????????????????????????
? Forge Conductor - 127.0.0.1:8092 ?
? supervisor - budget - arbitration - plan DAG ?
? ?? art director ?? vector operator ?? raster operator ?
? ?? print verifier ?? blind visual critic ?? memory curator ?
? ?? typed tool gateway (allowlist, roots, idempotency) ?
? ?? verifier (artifact/hash/gates/render) ?
? ?? episode ledger + eval/promotion ?
????????????????????????????????????????????????????????????????????????
? ? ?
/opt/craft CLI/MCP Postgres `forge` artifact store
VectorCraft/PhotoCraft episode/event/... SHA-256 + gate reports
?
/opt/pod-pipeline (deterministic, unchanged) - Fourthwall (approval only)
```


Plane boundaries

```
| Plane | Owns | Never owns |
|---|---|---|
| Console | read-only observation | agent loop, DB writes |
| `pod_pipeline` | deterministic asset run/publish steps | LLM planning, creative choice |
| DeerFlow | conversation, sessions, DeerMem facts, subagents, checkpoints | Craft command semantics, final quality verdict |
| **Forge** | task envelope, planning, tool calls, evidence, ledger, promotion | model weights, storefront authority |
| Craft apps | document truth, command semantics | agent memory |
```

3. Request lifecycle

1. **Brief** - user/operator/DeerFlow submits a `TaskEnvelope`.
2. **Preflight** - rights, app/version/catalogue hash, output contract, budget, approval needed.
3. **Retrieve** - bounded prior episodes/skills with the same app/version/task family.
4. **Plan** - command ids from the pinned catalogue; a gate per step; stop condition.
5. **Execute** - typed gateway; one step at a time on a copy; idempotency key; await every MCP reply.
6. **Verify** - process -> artifact/hash -> gates -> independent render -> tile/crop -> blind critic -> human rubric. Missing evidence = `UNVERIFIED`.
7. **Record** - append-only hash-chained episode and artifact index.
8. **Reflect** - only verified episodes; candidate lesson/skill with evidence ids.
9. **Promote** - calibrated horizon + Wilson LB > baseline + golden regression + human approval; pointer flip; rollback retained.
10. **Publish** - only after artifact-hash-bound approval; verify storefront read-back.

4. Integration map

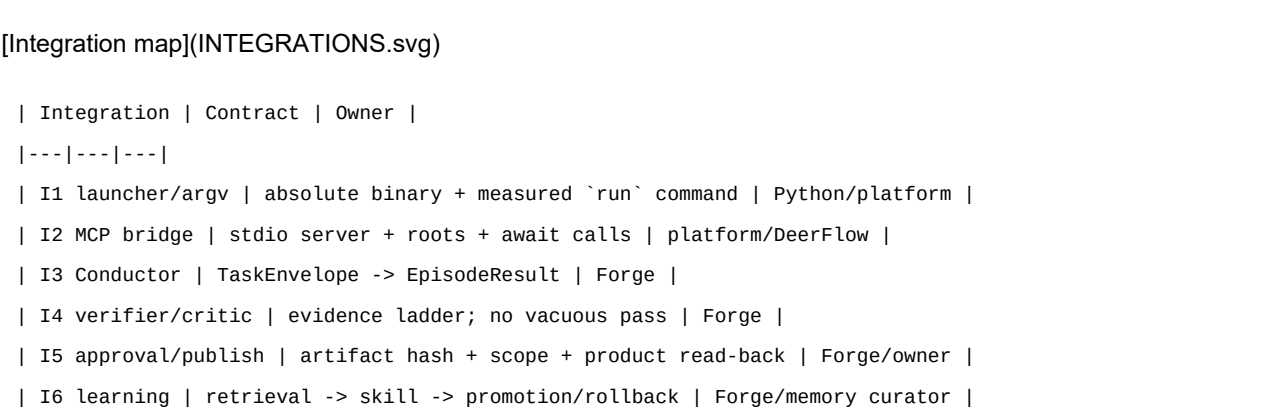

```
| Integration | Contract | Owner |
|---|---|---|
| I1 launcher/argv | absolute binary + measured `run` command | Python/platform |
| I2 MCP bridge | stdio server + roots + await calls | platform/DeerFlow |
| I3 Conductor | TaskEnvelope -> EpisodeResult | Forge |
| I4 verifier/critic | evidence ladder; no vacuous pass | Forge |
| I5 approval/publish | artifact hash + scope + product read-back | Forge/owner |
| I6 learning | retrieval -> skill -> promotion/rollback | Forge/memory curator |
```

5. Core data contracts

```
// TaskEnvelope
{"episode_id":"uuid","brief":"...","task_family":"ai_badge_trace",
"apps":[{"name":"VectorCraft","version":"0.21.1","catalogue_sha256":"..."}],
"rights":{"source":"...","licence":"..."},
"output":{"format":"svg","width":2400,"height":3000,"dpi":300},
"gates":["craft_trace"],"budget":{"max_steps":20,"max_seconds":900,"max_cents":100}}
```

```
// ToolCall (idempotent)
{"tool":"vectorcraft.run","cmd_id":"imageTrace.make","params":{},
"idempotency_key":"sha256(episode|step|params|input_hashes)","dry_run":false}

// VerificationVerdict
{"rungs":{"process":{"ok":true},"artifact":{"sha256":"..."},"gates":{"ok":true},
"render":{"ok":true},"tiles":{"ok":true},"critic":{"verdict":"pass"},
"human":{"score":4}},"verdict":"accepted|rejected|needs_human|unverified"}

// Skill (procedural memory)
{"skill_id":"vc-ai-badge-trace","version":3,"app":"VectorCraft",
"catalogue_hash":"...","preconditions":{},"steps":[],"gates":[],
"stats":{"success":8,"failure":1},"status":"candidate|active|rolled_back"}
```

6. State machines

Episode

`planned -> executing -> verifying -> accepted | rejected | needs_human | unverified | failed` with crash recovery via the queue lease and idempotent tool ledger. A failed gate is terminal for shipping; retry only named transient faults.

Skill

`draft -> candidate -> active -> superseded | rolled_back`

Promotion requires: declared evaluation horizon, Wilson lower bound above baseline, zero golden regression, human approval. **3/3 is not sufficient** (Wilson LB 0.4385; the original rule was rejected by simulation). Demotion must be tested: "2 failures in last 20" false-demoted a 95% skill 41% of the time; prefer/test 2-consecutive or 3-in-20.

Job

`queued -> leased -> running -> done | failed | queued (retry) | dead`

Lease has `lease_until`; a reaper requeues expired work; bounded scans; no duplicate side effect.

7. Evidence ladder (why each rung exists)

Rung	Proves	Failure mode it catches
process	command ran, result shape	missing result, wrong exit
artifact/hash/dimensions	exact bytes/size/DPI	file exists but wrong size
domain gates	white residual, specks, coverage, text, fills	traces/gates failing
independent render	engine vs rsvg/PDF	renderer drift
tile/crop metrics	localized defects	global SSIM misses 4% defect
blind critic	brief/hierarchy/type/colour	ungrounded "looks good"
human rubric	taste/print safety	proxy optimization

Measured: global SSIM caught 7/15; tile-min 13/15 but 3/4 false alarms; the 5-check composite

15/15 recall, 0/4 false alarms. White fringe is invisible on white; render on black **and** white.

8. Hosting

Component	Bind	Notes
console	`127.0.0.1:8091`	existing; viewer only
DeerFlow	existing containers	DeepSeek key via env name; no secret in repo
Forge conductor	`127.0.0.1:8092`	systemd, loopback only
Forge UI	`127.0.0.1:8093`	optional approval viewer
`pod-mcp`	should be `127.0.0.1:8765` + auth	current `0.0.0.0` is a finding
Postgres	local container	new `forge` DB/role; `pod` untouched
artifacts	local content-addressed store	hash + gate report + retention

Capacity: 2 vCPU/7.9 GB, 36 GB free, no GPU; <=2 episodes, one global Craft semaphore, daily cost cap, nightly dump + restore drill, no new public port.

9. Failure and refusal behavior

Condition	Response
app binary missing/stub	`E_TOOL_NOT_INSTALLED`; stop
unknown command id	`E_COMMAND_UNKNOWN`; no fallback invocation
path outside roots	`E_ROOT_DENIED`
missing document/selection	open/select; `enabled:false` is state
PhotoCraft interleaved calls	await each reply; do not pipe dependent calls
gate failed / vacuous	`failed`/`unverified`; no ship
`prep_print_art` warning-only upscale	parse `warnings`; refuse print above limit
source mutated	fail/quarantine
key missing/invalid	named refusal; no fake completion
cap exceeded	stop before spend; `E_BUDGET`
worker crash	lease expiry/requeue; idempotent replay
critic/gate disagree	`needs_human`; critic cannot override
publish without approval	`E_PUBLISH_NOT_APPROVED`
app/catalogue drift	pin; skill expired until revalidated

10. Rollback

- Phase 0: restore original launchers, `routes.py`, MCP config from backup.
- Phase 1: stop/disable `forge-*`; `DROP DATABASE forge`; `pod` untouched; artifact store retained.
- Phase 2: `FORGE_MEMORY=off`; active skill pointer flips to previous version.
- Every file change records pre-change SHA-256; rollback is a file/pointer restore.

11. Build sequence

Step	Work	Evidence
1	I1 launchers/argv	one trace + one retouch
2	I2 MCP registration	`tools/list` + batch
3	I3 DDL/service/queue	apply twice; 33 tests; replay

```
| 4 | I4 verifier/critic | composite fixture results |
| 5 | I5 approval/publish | approval reuse blocked; read-back |
| 6 | I6 retrieval/promotion | A/B + null result handling |
| 7 | 50 goldens/print/second app | measured quality/cost |
```

12. What this architecture refuses to hide

- It cannot drive Film/Design/Effect today; those are absent.
- It cannot train weights or do RL on this VPS.
- It cannot prove "better than human" without a blind study.
- It cannot publish safely until templates/approval are configured.
- It cannot claim a live key until the zero-spend metadata check is run.

Related: [`README.md`](README.md) - [`execution-wave/09-GOAL-GAP-PLAN.md`](execution-wave/09-GOAL-GAP-PLAN.md) - [`execution-wave/10-CLAIM-REGISTER.md`](execution-wave/10-CLAIM-REGISTER.md) - [`diagrams/`](diagrams/index.html)

Goal evaluation and research plan

Date: 2026-11-05 - **Status:** evaluation is current; implementation is not started.

Companions: [`GOALS.md`](GOALS.md) -
[`execution-wave/09-GOAL-GAP-PLAN.md`](execution-wave/09-GOAL-GAP-PLAN.md) -

[`execution-wave/10-CLAIM-REGISTER.md`](execution-wave/10-CLAIM-REGISTER.md).

1. What we set out to achieve

Build an AI agent that can design and ship real Craft work, learn from its runs, remember what

works, use the existing VPS + DeepSeek V4.1 Flash, and be truthful about its limits.

2. Goal-by-goal outcome

```
| Goal | Desired outcome | Current outcome | Status | Evidence |

|---|---|---|---|---|

| **G1** Execute Craft | run trace/retouch/print through the pipeline | execution path is stubs/argv; real
CLIs work standalone | **BLOCKED** | `01-EXECUTION-REPAIR.md`; S1/S3 |

| **G2** Native tools | typed CLI/MCP surface, no GUI guessing | 918/965 commands; 33/26 MCP tools; not
registered; no gateway | **PARTIAL** | S3; `02-FORGE-SKELETON` |

| **G3** Verify | artifact + gates + render + blind critic + human | gates exist but can be
vacuous/pre-artifact; no integrated critic | **PARTIAL** | S3; `03-VISUAL-DEFECTS`; `04` |

| **G4** Learn | improve from verified episodes, remember | no episode/eval/skill tables; DeerMem facts
only; L0 | **NOT STARTED (L0)** | S1; S6; `04-PROMOTION-SIM` |

| **G5** Host | run on the existing VPS/key | DeerFlow 2.2 + `deepseek-flash` running; 2 vCPU/no GPU; key
unverified | **FEASIBLE** | S1; S12 |

| **G6** Publish safely | human-approved, verified product | no approval queue; templates unset; no
autonomous publish | **BLOCKED** | S1; S12 |

| **G7** Truth | labels, claims, gaps, no invention | 400 answers, claim register, errata; README claim
still needs correction | **IMPROVING** | REPORT; 10-claim; ERRATA |
```

3. What we actually know

Verified

- The VPS is 2 vCPU / 7.9 GB / 36 GB free, no GPU/display.

- DeerFlow 2.2.0 runs `deepseek-flash` ("DeepSeek V4.1 Flash"), 1,048,576 ctx, 8,192 output.

- VectorCraft 0.21.1 and PhotoCraft 0.20.2 are installed; their MCP servers work standalone.

- `/opt/pod-pipeline/bin/*-cli` are stubs exiting 127; `routes.py` argv is invented.

- Only `forge` MCP (3 pipeline tools) is registered in DeerFlow.

- `pod` DB is empty; no episode/eval/skill tables.

- 39 skills, 400 answers, 8 diagrams, 6 examples, 131-file package.

- Adapter: 30/30 tests. Promotion sim: 23/23 tests. Visual composite: 15/15 with 0/4 false alarms

on the synthetic corpus.

Not verified / not true

- The DeepSeek key's live validity.

- The README's live E2E claim (historical/unreproducible now).

- FilmCraft/DesignCraft/EffectCraft availability.

- Real gate/human rates, human inter-rater agreement, cost per accepted artifact.

- "The agent learns art direction" and "better than a human designer."

- A production DDL migration or live deployment.

4. What is possible now

1. **Fix the execution path** on a staging copy; run one real trace and one retouch; capture artifacts.

2. **Register the Craft MCP servers** and prove `tools/list`/`command_batch`.

3. **Run the Forge skeleton** DDL/tests against a scratch Postgres; prove duplicate/refusal/crash.

4. **Run the visual critic** on the 19-case synthetic corpus; require 15/15 and 0/4.

5. **Run the promotion simulation** and choose a policy; 3/3 is not a policy.

6. **Validate the key without spend** via `/user/balance` and `/models`.

5. What is not possible on this VPS now

- Driving FilmCraft/DesignCraft/EffectCraft: not installed.

- Fine-tuning/RL: API model, no GPU/open weights/corpus.

- Pixel-first GUI automation: no display; control bridge missing a library.

- Autonomous publish: no approval queue; template ids unset.

- A claim of artistic superiority: no blind study.

6. The best path (decision)

DeerFlow 2.2 as front door/runtime + Forge Conductor as a third plane + native Craft CLI/MCP + Postgres ledger/queue + DeerMem facts + versioned skills. Do not build a new generic harness; do not start with GUI or training; do not make the pipeline the agent.

7. Research continuation plan

These are new questions, not repeats of the 400.

#	Question	Method	Output	Stop condition
R1	Does the repaired launcher/argv execute a real trace?	staging copy + real CLI; artifact + JSON	`R1-RESULT.md`	first missing artifact
R2	Can DeerFlow load a stdio MCP server with roots?	register + `tools/list` + batch	`R2-RESULT.md`	handshake failure
R3	Does DDL apply twice and enforce transitions?	scratch PG16 + duplicate/refusal tests	`R3-RESULT.md`	SQL assertion fail
R4	Does the visual composite generalize?	new photographic/gradient corpus + human labels	`R4-RESULT.md`	false alarm > budget
R5	What promotion policy is defensible?	simulate n/k/p0, then real episodes	`R5-RESULT.md`	no separation from null
R6	Does retrieval improve first-attempt pass?	A/B 10-50 goldens, two arms	`R6-RESULT.md`	no gain -> disable
R7	Does the blind critic agree with humans?	blind ratings, precision/recall	`R7-RESULT.md`	low agreement -> needs_human
R8	What is the real cost per accepted artifact?	usage ledger + balance delta	`R8-RESULT.md`	budget cap exceeded
R9	Is the key valid without spend?	`/user/balance` + `/models`	`R9-RESULT.md`	401/402

| R10 | Can publish be made safe? | approval bind + read-back | `R10-RESULT.md` | any unapproved write |

8. Re-evaluation rule

Re-run this evaluation after every phase. A goal moves from `BLOCKED/PARTIAL` to `ACHIEVED` only when the named gate has a reproduced command/output and the claim register is updated. A null result is a valid outcome; a design is not an achievement.

9. Current verdict

Research/design: strong. Execution: blocked at Phase 0. Learning: not started. Product: feasible narrowly (VectorCraft + PhotoCraft) once the execution path and approval are real.

Plain English - what we have, what is wrong, and what we are building

This is the explanation for a human who does not want to read four hundred questions and a dozen evidence files. It is intentionally blunt. If something is not built, it says so.

1. What we are trying to do

We want an AI worker that can make real print/vector artwork using the Craft apps that already run on the server, check its own work with evidence, remember what worked, and get better under human supervision. It should be able to take a brief like "make this badge trace-ready and print-safe," choose the right Craft commands, produce an SVG/PNG/PDF, verify the size/DPI/colors/gates, show the result to a person, and only then publish.

That is the product. It is not "an AI that replaces the artist." It is a reliable production assistant with a paper trail.

2. What already exists

The server already runs **DeerFlow 2.2**, an agent runtime, with the **DeepSeek V4.1 Flash** model. DeerFlow can hold conversations, run subagents, remember facts across sessions, and connect to tools. That part is real.

The server also has **VectorCraft 0.21.1** and **PhotoCraft 0.20.2** installed. They are real Rust apps with 918 and 965 commands and 33/26 MCP tools. They are independent apps, not Adobe clones.

There is a console at port 8091 and a small pipeline that is supposed to run the apps, verify the image, and publish to Fourthwall. There are 39 skills, 400 research answers, 8 diagrams, and six worked examples.

That is a lot of real material. But having the parts is not the same as having a working machine.

3. What is actually broken

The pipeline is connected to **fake launchers**: the scripts under `/opt/pod-pipeline/bin` are tiny stubs that exit with code 127. The real Craft binaries are elsewhere and are never reached.

The Python `routes.py` also calls the apps with commands that do not exist. It pretends there is a `trace` subcommand and an `--input` argument. The real apps use `run --in ... --cmd ... --export ...`. So even if the stubs were replaced, the arguments would still fail.

The Craft MCP servers work when you start them by hand, but DeerFlow is not registered to use them. The only MCP server DeerFlow knows about is the old three-tool pipeline server.

The database is empty. There is no table that records an episode, a tool call, a gate result, a critique, an evaluation, or a skill. So the system cannot learn from its runs, because it does not

remember them.

There is no approval queue. The storefront product ids still contain `REPLACE_WITH_TEMPLATE_ID`. Publishing is therefore not safe and not configured.

Finally, the README says a live end-to-end run succeeded. That is not true today: the database is empty and the last real run failed at the first stub. Treat that sentence as history, not current status.

4. What we did about it

We did not start by rewriting the product. We did five things:

1. **Measured the real commands.** We ran the actual VectorCraft and PhotoCraft binaries and recorded the exact argv that works, including the fact that VectorCraft does not create export folders and PhotoCraft does.
2. **Designed the conductor.** We designed a third control plane, "Forge Conductor," that sits beside the console and the pipeline. It owns planning, tool calls, evidence and learning; it does not own the Craft apps' document truth or the model weights.
3. **Built executable evidence.** A 13-table Postgres schema, a 36-edge state machine, 33 Python tests, an adapter with 30 tests including a real crash/kill test, and a visual corpus with 15 defects and 4 controls.
4. **Corrected our own mistakes.** The original promotion rule ("3 successes + Wilson 0.60") cannot work: 3/3 gives a lower bound of 0.4385. The simulation replaced it with a horizon-based policy, and we wrote the correction into the skills instead of hiding it.
5. **Packaged everything.** The corpus, skills, examples and diagrams are in a 131-file Desktop folder and mirrored into the vault, with hashes and an index. Nothing was deleted.

5. The six integrations, in plain terms

I1 - Fix the launchers and commands. Point the pipeline at the real apps and use the commands that actually exist. This is the first thing to build. Without it, nothing else can run.

I2 - Connect the real Craft MCP servers. Register VectorCraft and PhotoCraft with DeerFlow, give them explicit read/write folders, and wait for each call to finish. PhotoCraft can interleave calls; a dependent call must not be fired blindly.

I3 - Add the conductor. A small service that receives a task, makes a plan, runs the steps, records everything, and can recover after a crash. It uses the new Postgres tables and a queue.

I4 - Add the verifier and blind critic. A step is not done because the command exited 0. The verifier checks the file hash, dimensions, DPI, gates, a separate render, tile/crop differences, and a critic that sees the image without knowing which version is supposed to be better. Missing evidence means "unverified," not "pass."

I5 - Add human approval before publish. Approval is tied to the exact artifact hash. A stale approval cannot be reused. The storefront product/template is checked before any write. No autonomous publishing.

I6 - Add learning and evaluation. Episodes become searchable cases; repeated success can become a versioned skill; a skill is promoted only after a declared number of trials, a Wilson lower bound above baseline, a golden regression check, and human approval. A null A/B result disables the memory. No fine-tuning or RL on this server.

6. The eight Python changes, in plain terms

1. Rewrite `routes.py` to call the measured commands.
2. Add a preflight that checks "is the app installed, is the version/catalogue pinned?" and refuses by name if not.
3. Fix `craft_trace` so the text check cannot pass on zero boxes and the artifact is not saved before the gate passes.
4. Fix `prep_print_art` so `ok:true` is not treated as a pass and a 3.6x upscale is not silently called print-safe.
5. Hash the source before and after; fail if the run mutated the original.
6. Add idempotency and duplicate replay to the tool gateway/DB.
7. Add a worker lease and reaper so a crash requeues work exactly once.
8. Record token/cost per step and enforce a cap.

These are small, testable changes. They are not a rewrite.

7. The eight agent/skill changes, in plain terms

1. The Craft operator must attach evidence, not say "looks good."
2. The learning skill must use calibrated promotion and tested demotion, not 3/3.
3. The visual critic must use the five-check composite and render on black and white.
4. The harness architect must check which apps exist before designing for them.
5. The code adapter must record donor provenance and not copy code verbatim.
6. The research navigator must point to the right slice of the 400 answers without flooding context.
7. The MCP skill must wait for dependent calls and be honest about stdio vs HTTP.
8. The print/publish skill must bind approval to the artifact hash and check rights/templates.

8. What the goals are - and where they stand

- **Execute Craft work:** blocked. The stubs and wrong arguments stop it.
- **Use native tools:** partial. The MCP servers exist; they are not registered.
- **Verify quality:** partial. Gates exist but can lie; the critic is not wired in.
- **Learn:** not started. There is no episode/eval/skill data.
- **Host on the VPS:** feasible. The runtime and model are there; it is constrained.

- **Publish safely:** blocked. No approval, no template ids.
- **Be truthful:** improving. We have a claim register and an errata file; the old README sentence still needs correcting in the product docs.

9. What is possible, and what is best

Possible now: fix the execution path, run one real trace and one real retouch, record the evidence, build the ledger and queue, run the visual critic on the synthetic corpus, and validate the key without spending money.

Not possible now: all five Craft apps (three are absent), autonomous publishing, training new model weights, RL, GUI-first automation (no display), or proving "better than a human."

Best path: fix I1 and I2 first, then I3 and I4. Do not start with a GUI agent, a training run, or a redesign. The bottleneck is the execution path, not the model.

10. What we need from Riley

1. Approve Phase 0 and let the repair be applied to a **staging copy** first.
2. Approve the zero-spend key check (`/user/balance`, `/models`); do not use a chat completion as a key test.
3. Decide whether FilmCraft/DesignCraft/EffectCraft will be purchased; until then they are out of scope.
4. Set the Fourthwall template/area ids or confirm publish stays disabled.
5. Choose the promotion baseline (`p0`), the evaluation horizon (`n`) and the false-promotion budget; the simulation is a suggestion, not a policy.
6. Name the human approver for taste/print/publish.

11. The honest bottom line

We have a strong research base, a real runtime, a real command catalogue, a real execution plan, and working prototype tests. We do **not** have a working end-to-end Craft agent yet. The first honest milestone is one real trace and one real retouch, recorded with evidence. After that, the learning and publishing layers are worth building.

12. Where to read more

- [`README.md`](README.md) - the map and the plans.
- [`ARCHITECTURE.md`](ARCHITECTURE.md) - the system design.
- [`GOALS.md`](GOALS.md) - goals and non-goals.
- [`GOAL-EVALUATION.md`](GOAL-EVALUATION.md) - goal-by-goal status.
- [`execution-wave/09-GOAL-GAP-PLAN.md`](execution-wave/09-GOAL-GAP-PLAN.md) - the decision-complete plan.
- [`execution-wave/10-CLAIM-REGISTER.md`](execution-wave/10-CLAIM-REGISTER.md) - what is proven.

- [`diagrams/index.html`](diagrams/index.html) - eight pictures.
- [`PDF-CATALOGUE.md`](PDF-CATALOGUE.md) - the PDF reading copies.

Forge Conductor - Goals, Integrations and Decision Plan

Derived reading copy. Markdown remains the source of record. No source file is modified by this build.

GOALS - the durable focus for this program

Status: authoritative for the research/implementation program. Read this before any plan or code.

Date: 2026-11-05 - **Owner:** Riley - **Program:** DeerFlow Forge / Forge Conductor.

Mission

Build a **hosted, auditable design-production agent** that can take a brief, use the installed Craft apps through their native command/MCP surfaces, verify its own output with hard evidence, remember what worked, and ship only what a human has approved.

It is not "a chatbot that talks about design." It is a production operator with a ledger.

Product outcome (what exists when this succeeds)

A user can submit a print/vector/web brief to **Forge Conductor**. It:

1. selects the right app and exact command ids from the pinned catalogue;
2. runs on a copy, records every action and artifact;
3. verifies dimensions, DPI, colour, gates and a blind visual review;
4. refuses or asks a human when evidence is missing or the taste call is unresolved;
5. stores a case/skill candidate from the run;
6. promotes a procedure only after repeated verified success + regression + human approval;
7. never autonomously publishes to the storefront.

Non-negotiable goals

ID	Goal	Success test
G1	Execute the installed Craft apps reliably	one VectorCraft trace and one PhotoCraft retouch run from the pipeline path, with expected artifacts
G2	Use native commands/MCP, not blind clicking	every action is a catalogued command id or a justified browser fallback
G3	Verify with evidence	artifact hash + dimensions/DPI + gates + independent render + blind critic + human where applicable
G4	Remember and improve truthfully	L1/L2 ledger/retrieval/skills; A/B shows gain or is disabled
G5	Host on the existing VPS/model	loopback services, 2 vCPU budget, DeepSeek key by env name, no new public port
G6	Keep humans on taste/publish	approval is required for print/publish and skill activation
G7	Be honest about limits	VERIFIED/READ/INFERRED/UNVERIFIED labels; no "better than human" claim without a study

Non-goals / explicit boundaries

- **No claim** that the agent is better than a human designer; target is a reliable production operator under human art direction.
- **No weight training, fine-tuning or RL** in Phases 0-2; no GPU/open weights on this VPS.
- **No autonomous publish** or storefront mutation.
- **No fake 1:1 Adobe compatibility**; the Craft apps are independent implementations.

- **No all-app claim** until FilmCraft/DesignCraft/EffectCraft are installed and catalogued.
- **No GUI-first agent** while there is no display/GPU and the control bridge is broken.
- **No unverified success** - exit 0, `ok:true` or a screenshot alone is not proof.

Scope (current)

```
| In scope | Out of scope (now) |
|---|---|
| VectorCraft 0.21.1 | FilmCraft (not installed) |
| PhotoCraft 0.20.2 | DesignCraft / EffectCraft (not installed) |
| Native CLI + MCP | Pixel-only desktop automation |
| Print/vector/raster verification | CMYK press proof without vendor proof |
| L1/L2 memory and skills | L3/L4 training/RL |
| Human-approved publish | Autonomous publish |
```

Success metrics

- First-attempt verified-pass rate on held-out goldens.
- Attempts per accepted artifact.
- Human rework minutes.
- Cost/tokens per accepted artifact.
- Unsafe publishes = **0**.
- Source mutations = **0**.
- Promotion uses a pre-declared evaluation horizon and Wilson lower bound above baseline; a 3/3 sample is a minimum, not proof (3/3 LB ? 0.4385).
- Every accepted artifact has a complete evidence chain.

Invariants

1. Work on copies; never overwrite the source/master.
2. Exact command id from the pinned catalogue; unknown id -> stop.
3. A failed gate is terminal for shipping; never edit a report to pass.
4. A screenshot or exit 0 can only downgrade confidence, never certify.
5. Memory is data, not instructions; no tool-scope expansion from retrieval.
6. A skill is promoted only by evidence + regression + human approval; rollback exists.
7. Secrets never enter prompts, logs, ledger, repo or screenshots.
8. The `pod` DB/pipeline remains deterministic; Forge may call it, not absorb it.

Current truth (2026-11-05)


- VPS has 2 vCPU/7.9 GB, no GPU/display; DeerFlow 2.2 runs `deepseek-flash` (V4.1 Flash), key by env name only; key validity unverified.
- VectorCraft/PhotoCraft installed; Film/Design/Effect absent.
- `/opt/pod-pipeline/bin/*-cli` are stubs exiting 127; `routes.py` argv is invented; Craft MCP is not registered in DeerFlow.

- `pod` DB empty; no learning/eval tables; console is a viewer.

- 39 skills, 400 answers, six examples, eight diagrams - research/design, not deployed.

Decision log

Date	Decision
2026-11-05	Use DeerFlow 2.2 + DeepSeek as substrate; build a third `forge-*` plane, not a new harness
2026-11-05	Phase 0 fixes execution (shims/argv/MCP) before any agent feature
2026-11-05	L1/L2 only; no fine-tune/RL; no autonomous publish
2026-11-05	Target = reliable production operator under human direction, not "better than human"
2026-11-05	Promotion calibration: 3/3 is not sufficient; declare horizon + Wilson baseline; demotion/regression suite must be tested (task-11)

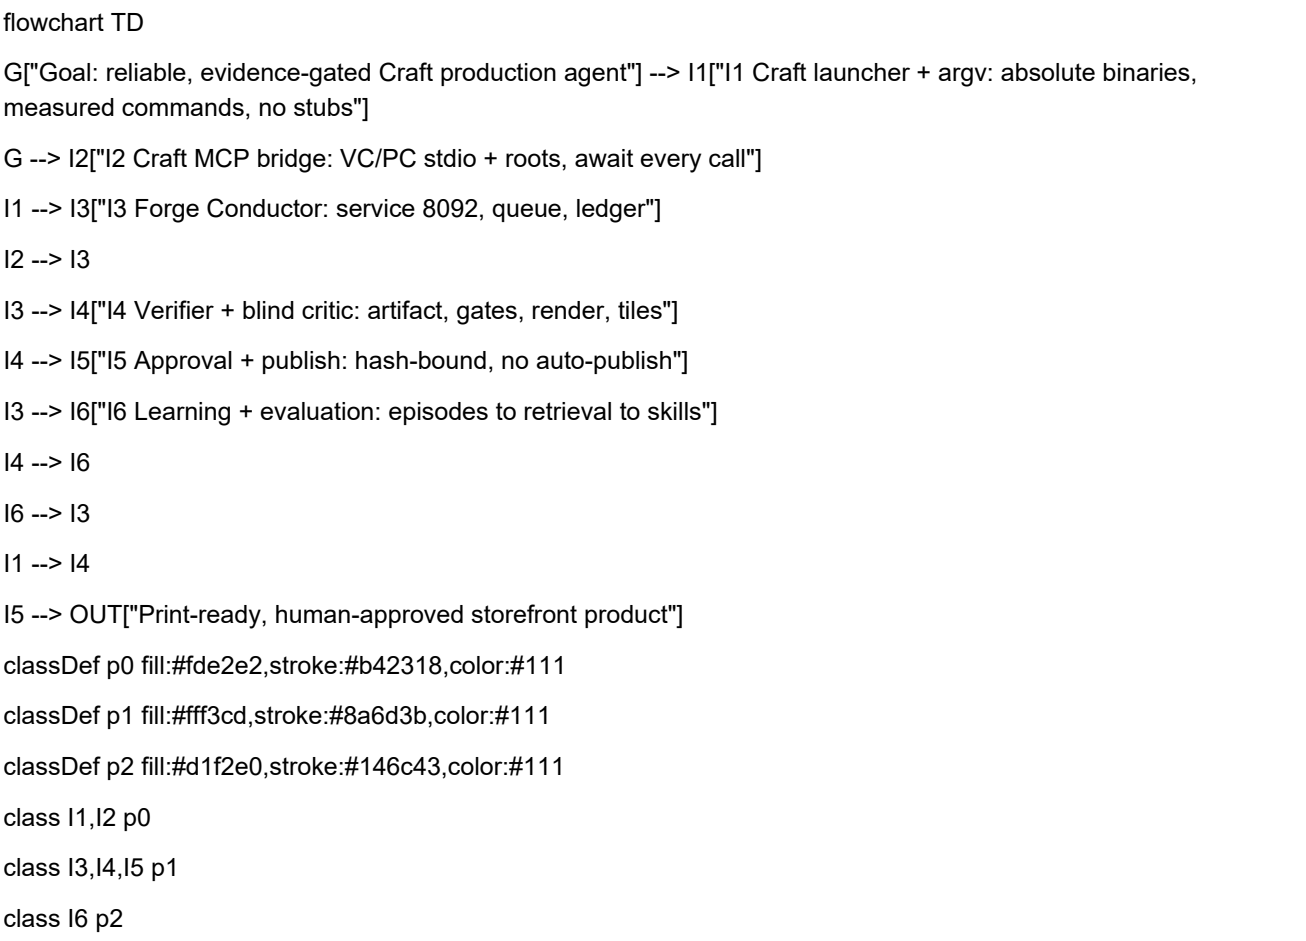
flowchart TD
G["Goal: reliable, evidence-gated Craft production agent"] --> I1["I1 Craft launcher + argv: absolute binaries, measured commands, no stubs"]
G --> I2["I2 Craft MCP bridge: VC/PC stdio + roots, await every call"]
I1 --> I3["I3 Forge Conductor: service 8092, queue, ledger"]
I2 --> I3
I3 --> I4["I4 Verifier + blind critic: artifact, gates, render, tiles"]
I4 --> I5["I5 Approval + publish: hash-bound, no auto-publish"]
I3 --> I6["I6 Learning + evaluation: episodes to retrieval to skills"]
I4 --> I6
I6 --> I3
I1 --> I4
I5 --> OUT["Print-ready, human-approved storefront product"]
classDef p0 fill:#fde2e2,stroke:#b42318,color:#111
classDef p1 fill:#fff3cd,stroke:#8a6d3b,color:#111
classDef p2 fill:#d1f2e0,stroke:#146c43,color:#111
class I1,I2 p0
class I3,I4,I5 p1
class I6 p2

09 - Goal-to-Code Gap Audit and Decision-Complete Plan

Date: 2026-11-05 - **Status:** PLAN, not implementation. No production file/DB/service changed. **Inputs:** `GOALS.md`, first `REPORT.md`, `wave2/08-200-QUESTIONS.md`, `wave2/01`-`07`, execution-wave plan, live VPS probes, local source. **Lens:** goal -> research -> code -> product -> operations.

1. Outcome

A hosted **Forge Conductor** on the existing DeerFlow 2.2/DeepSeek runtime that can execute a brief on VectorCraft/PhotoCraft through exact CLI/MCP commands, verify the artifact and gates, record an evidence-grade episode, propose only verified lessons, and require human approval to publish. The first release is a **production operator**, not an autonomous artist and not a new generic harness.

What users can do after Phase 1 that they cannot do now: submit a brief, watch a real trace/retouch run end-to-end, inspect the artifact hash + gates + blind critique, and reproduce the run from the ledger - with no stub, no invented argv and no fake success.

2. Current behavior (evidence, no assumptions)

#	Current behavior	Evidence	Status
C1	Pipeline cannot execute any Craft step	`/opt/pod-pipeline/bin/*-cli` 122-127 B shims exit 127; last run failed there	`VERIFIED`
C2	The argv contract is invented	`routes.py:73-80` (`trace`, `--input`, `--svg-out`) and `:88-96` (`--input` for PhotoCraft); real CLIs reject them	`VERIFIED`
C3	Only two Craft apps are installed	VectorCraft 0.21.1 / PhotoCraft 0.20.2; Film/Design/Effect absent host-wide	`VERIFIED`
C4	Craft MCP is not registered in DeerFlow	only `mcpServers.forge` exists; craft MCP handshakes work standalone	`VERIFIED`
C5	DeerFlow 2.2 + DeepSeek run on the VPS	backend 2.2.0; `deepseek-flash`/"V4.1 Flash", 1M ctx, 8k output; key by env name	`VERIFIED` config; key validity `UNVERIFIED`
C6	No learning/eval ledger exists	`pod` has 5 tables, no episode/action/skill/eval; DB empty	`VERIFIED`
C7	Console is a viewer	pure viewer at 127.0.0.1:8091; no job controls/auth	`VERIFIED`
C8	README's live E2E claim is not reproducible now	`README.md:191-194`; DB empty and stub failure; it may be historical	`HISTORICAL/UNREPRODUCIBLE`
C9	Gates can lie if read naively	`craft_trace:344` saves before gates; `:250` vacuous retype gate; `prep_print_art:356` `ok:True` with warning-only upscale	`READ` + prior probes
C10	MCP endpoint is host-sensitive	`pod-mcp` 0.0.0.0:8765, unauthenticated, pod in Docker group	`VERIFIED`
C11	39 skills/400 answers are instructions, not runtime	installed skills; pipeline has no LLM/loader	`VERIFIED`
C12	Foreign `AGENTS.md`	Grok App Builder contract (`/workspace`, port 8080) not this VPS	`READ`

2.1 Measured Phase 0 contracts (do not revert to the old ASSUMPTIONs)

Contract	Measured behavior
VectorCraft trace	`run --in F --cmd select.all --cmd imageTrace.make --params '{"params":{...}}' --cmd imageTrace.expand --export out.svg` -> exit 0, `{"result":{"bytes":334,"format":"svg"},"step":"export"}`; PDF export also works; **export does not create parent dirs** (`os error 2`)
PhotoCraft run	`run <FILE|--new> --cmd ID --params J --out F`; opens traced SVG with a benign flatten warning; `image.trim` 161x121; `image.imageSize` at 300 ppi; creates parent dirs

| VectorCraft MCP | `mcp --headless --automation-read-root ... --automation-write-root ...` |

| PhotoCraft MCP | `mcp` **without `--headless`**, same roots; dependent calls must be awaited (server can interleave) |

| Gateway/binary | gateway uid 0, glibc 2.36 >= binaries' max GLIBC_2.35; bind mount is viable |

| Security | `POD_MCP_HOST=0.0.0.0` in `pipeline.env` overrides code default `127.0.0.1`; rebind is one value. Key validation: `GET /user/balance` + `GET /models` with Bearer; 200 valid, 401 invalid, 402 no balance; **never** use a chat completion as a key test |

| Visual defect | global SSIM catches 7/15; tile-min catches 13/15 but flags 3/4 clean controls; region SSIM catches 11/15 with 0/4 false alarms - combine region + tile + crop, not one threshold |

3. Goal->code gap matrix

| Goal | Research says | Code/runtime reality | Gap | Severity | Owner |

|---|---|---|---|---|---|

| G1 execute Craft | real 918/965 registries, MCP works | stubs, wrong argv, MCP unregistered | execution path broken | **P0** | task-8 |

| G2 native tools | use CLI/MCP, not GUI | no gateway; GUI bridge broken | no typed tool surface | **P0** | task-9/13 |

| G3 verify | six-rung evidence ladder | gates exist but can be vacuous/pre-artifact; no critic | no verifier/critic integration | **P0** | task-10 |

| G4 learn | L1/L2 buildable, L3/L4 not | no ledger/eval/retrieval/skill tables | no learner | **P1** | task-11 |

| G5 host | VPS capacity, model exists | 2 vCPU/7.9 GB; key unverified; no GPU | capacity/key risk | **P1** | task-12 |

| G6 approval | human gate | no approval table/queue; publish config unset | no safe publish | **P0** | task-9/12 |

| G7 truth | labels/evidence | README claim drift; foreign AGENTS | documentation must be corrected | **P1** | Lead |

| All apps | only VC/PC installed | Film/Design/Effect absent | scope must exclude | **P1** | Lead |

| Better-than-human | no benchmark | no eval | claim must be dropped | **P0** | Lead |

4. Decisions (rejected alternatives)

| # | Decision | Rejected | Why |

|---|---|---|---|

| D1 | DeerFlow 2.2 is the runtime/front door | build a new harness; use Eko as core | already hosted, MIT, memory/subagents/checkpoints; Eko is dormant/JS/in-memory |

| D2 | Build a **third `forge-*` plane** | embed LLM in pipeline/console | preserves deterministic pipeline and replaceable agent |

| D3 | Phase 0 fixes execution first | build ledger/agent first | without real commands, every downstream test is fake |

| D4 | VC + PC only for MVP | all Craft apps | others absent; claiming otherwise is false |

| D5 | Native CLI/MCP only in MVP | GUI/computer-use first | no display/GPU; bridge panics; commands are deterministic |

| D6 | Postgres `forge` DB + queue | new broker; reuse `pod` DB | one DB, no new service, `pod` untouched |

| D7 | L1/L2 memory + skills; promotion calibrated (no 3/3 shortcut) | fine-tune/RL now | API model, no GPU, no corpus/eval; simulation shows 3/3 LB 0.4385, so horizon + baseline required; claim discipline |

| D8 | Human-approved publish | autonomous publish | irreversible external side effect; template ids missing |

| D9 | Blind critic + crop evidence | one global SSIM/screenshot | measured 4% defect changes SSIM only 0.99994->0.9787 |

| D10 | Use donor mechanisms, original adapters | copy/vendor whole repos | maintenance/licence/verifiability; no verbatim code |

5. File-by-file change (planned; no production edit in this task)

5.1 Phase 0 - execution repair

| Path | Change | Test |

|---|---|---|

| `blueprint/files/deploy/craft-bin/*-cli` | replace 127 shims with launchers to `/opt/craft/*/bin` (absolute); keep refusal if absent | `--version` for VC/PC; absent app -> named refusal |

| `blueprint/files/pod_pipeline/routes.py:73-80` | replace trace argv with `run --in {src} --commands {steps} --export {svg}` or dedicated wrapper | one real trace; artifact exists |

| `blueprint/files/pod_pipeline/routes.py:88-96` | replace PhotoCraft `--input` contract with `photocraft-cli run FILE ... --out` | one real retouch |

| DeerFlow `extensions_config.json` | register vectorcraft/photocraft MCP stdio with roots; no arbitrary host paths | `tools/list`, `command_batch` |

| `README.md:188-211` | relabel live-E2E as historical/unreproducible; state current blockers | doc read-back |

| `AGENTS.md` | replace foreign Grok contract with a DeerFlow Forge/VPS contract, or remove | no port-8080 claims |

5.2 Phase 1 - Forge skeleton

| Path | Change |

|---|---|

| `blueprint/files/forge/contracts.py` | TaskEnvelope, ArtSpec, Handoff, ToolCall, Artifact, Verdict (versioned) |

| `blueprint/files/forge/gateway.py` | absolute binary registry, allowlist/roots/idempotency/refusals |

| `blueprint/files/forge/verifier.py` | artifact hash/dimensions/DPI + gate-report parser + read-back |

| `blueprint/files/forge/jobs.py` | Postgres queue `FOR UPDATE SKIP LOCKED`, leases, attempts |

| `blueprint/files/sql/schema_forge.sql` | new `forge` DB tables: episode/event/handoff/tool_call/artifact/gate/critique/eval/skill/job/budget/role |

| `blueprint/files/forge/critic.py` | blind prompt/schema, crop grounding, cannot-assess path |

| `blueprint/files/forge/memory.py` | episode append, bounded retrieval, candidate lessons |

| `blueprint/files/forge/promotion.py` | Wilson bound, N>=3, regression, approve/rollback |

| `deploy/systemd/forge-conductor.service` | loopback 8092, `ProtectSystem=strict`, env file |

| `deploy/systemd/forge-worker.service` | queue worker, <=2 concurrency, one craft semaphore |

| `deploy/systemd/forge-ui.service` | optional 8093 operator approval UI (loopback) |

5.3 Phase 2 - learning and evaluation

| Path | Change |

|---|---|

| `blueprint/files/forge/eval.py` | golden runner, A/B arms, metrics, JSON report |

| `blueprint/files/forge/evaluation/` | 10-50 golden fixtures (rights-cleared) |

| `blueprint/files/skills/*` | the five research skills + operator; loaded by agent, not pipeline |

| DeerFlow memory config | keep DeerMem for facts; Forge ledger for episodes/skills; do not duplicate |

5.4 Never change

`pod` schema, orchestrator determinism, console viewer contract, Craft app binaries/catalogues,

publish without approval, any secret value in repo/logs.

6. Failure modes and required behavior

| Failure | Required behavior |

|---|---|

| Missing/stub binary | named `E_APP_UNAVAILABLE`; no fallback that pretends success |

| Wrong argv/unknown id | `E_COMMAND_UNKNOWN`/`E_PARAM_REJECTED`; stop |

| No document/selection | open/select first; `enabled:false` is state, not absence |

| PhotoCraft concurrent MCP | await each reply; never pipe dependent calls |

| Artifact exists but gate failed | `failed`; preserve artifact for diagnosis; no ship |

`prep_print_art.ok` true with warning	parse `warnings`; over-2.5x upscale is a refusal for print
Text gate with 0 boxes	`unverified`, not pass
Source mutated	fail episode; quarantine
Key missing/invalid	named refusal; no fake completion; owner-approved live test
Budget exceeded	stop before spend; `E_BUDGET`
Worker crash	lease expiry/requeue; idempotent tool key; no duplicate publish
Critic/gate disagree	`needs_human`; never critic override
Publish without approval	refuse; `E_PUBLISH_NOT_APPROVED`
App/catalogue drift	pin hash; skill expired until revalidated

7. Tests (discriminating, including error paths)

Test	Command / evidence	Pass
T0 versions	`vectorcraft-cli --version`, `photocraft-cli --version`	expected versions
T1 trace	real 1024? badge via `craft_trace`/run	SVG/PNG + report, `ok:true`, 10 gates
T2 retouch	PhotoCraft crop->filters->imageSize on copy	2400x3000, 118.11 px/cm
T3 MCP	initialize -> tools/list -> command_batch	33/26 tools; batch result
T4 refusals	unknown id/outside root/missing doc	named codes; no write
T5 duplicate	same idempotency key twice	one effect, same result
T6 crash/resume	kill worker mid-episode	lease requeue; no duplicate
T7 verifier	fixture with failed gate	`failed`, not ship
T8 critic	labelled defect set	precision/recall + false-pass reported
T9 promotion	calibrated horizon (e.g. n=8, k>=7, LB>p0) + regression + human	simulation shows null-promotion rate and retention; 3/3 rule rejected; no overclaim
T10 packaging	copy corpus/skills	links/JSON/validation clean
T11 docs	README claims	no unreproducible "live E2E"

8. Rollback

- **Phase 0:** restore original `deploy/craft-bin` shims, `routes.py`, DeerFlow MCP config from backup; no DB migration.
- **Phase 1:** stop/disable `forge-*` units; `DROP DATABASE forge`; artifacts remain content-addressed; `pod` untouched.
- **Phase 2:** feature flag `FORGE_MEMORY=off`; retrieval/skills disabled; prior skill versions retained.
- Every file change has a pre-change SHA-256; rollback is a pointer/file restore, not a rewrite.
- If a live key test was approved, record spend; rotate the key if exposed.

9. Out of scope / blockers

- FilmCraft/DesignCraft/EffectCraft not installed; no command claims.
- GUI/computer-use blocked by missing display and broken control bridge.
- No fine-tune/RL (API model, no GPU/open weights/corpus).
- No autonomous publish; template ids missing.
- DeepSeek key validity not proven without an owner-approved live call.
- No "better than human designer" claim; no blind study.
- Adobe tutorials not executed; 50-task corpus is a proposal.

- Production migration/implementation is **not** authorized by this plan.

10. Diagram index (validated via Kroki)

Diagram	Purpose	Source
`01-goal-gap`	goals -> code gaps -> phases	`diagrams/01-goal-gap.mmd`
`02-runtime-topology`	VPS services/ports/planes	`02-runtime-topology.mmd`
`03-craft-command-path`	operator -> gateway -> CLI -> verifier -> critic	`03-craft-command-path.mmd`
`04-forge-architecture`	roles, memory, tools, data	`04-forge-architecture.mmd`
`05-learning-state`	episode/skill/rollback state machine	`05-learning-state.mmd`
`06-evidence-ladder`	why each proof rung matters	`06-evidence-ladder.mmd`
`07-decision-tree`	build-vs-buy / scope choices	`07-decision-tree.mmd`
`08-roadmap`	phase gates/time	`08-roadmap.mmd`

11. Open questions only the owner can answer

1. Is the live DeepSeek key valid, and may we spend a minimal completion to prove it? **Preferred: use the zero-spend metadata check first** (`GET /user/balance`, `GET /models`); a chat completion is not a key test.
2. Which Craft app is the first commercial target: VectorCraft or PhotoCraft?
3. Are FilmCraft/DesignCraft/EffectCraft available from a private artifact store, or out of scope?
4. Who is the human approver for print/publish and skill promotion?
5. What are the rights for the first 10/50 golden assets?
6. Is "Harness 2" the Google Harness? project, or an internal second harness? (terminology)
7. Is the desired interface chat-only, or an operator UI with approvals?
8. What is the cost ceiling per artifact/day?

Verdict

The product is buildable now only as a narrow, evidence-gated operator (VectorCraft + PhotoCraft). The model and harness already exist; the blockers are execution wiring, verification, ledger/approval, and scope honesty. Phase 0 must fix the execution path before any "learning" work is meaningful.
